
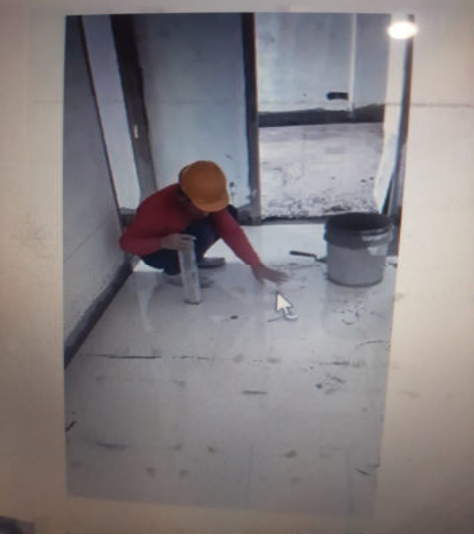



Date:-03-03-2025
(MONDAY)

Sikka Kaamya Project

Progress Report for the period 24-02-2025 to 02-03-2025

Tower Name	Tower Photo	Item	Progress of work
DIAMOND		RMC/Steel	10th floor roof slab - R/F work in progress
		Paint	Internal paint to start this week
		Tiling	1st floor completed
		Plumbing	1st floor completed
		Electrical	Yet to start
		M.S. Railings	Yet to start
		Internal Plaster	5th floor in progress
		External Plaster	N/A
		Fire Fighting	Yet to start
RUBY		RMC	Structure Work Completed
		Paint	Intenal putty work completed, external primer done 60%
		Tiling	Floor Tiling at 20th floor in progress
		Plumbing	Internal water supply and drainage work completed
		Electrical	Conduit work completed, wiring work yet to start
		M.S. Railings	Balcony railing completed and staircase railing in progress
		Internal Plaster	Completed
		External Plaster	94% completed
		Fire Fighting	Internal sprinkler system piping completed
OPAL		RMC	Structure Work Completed
		Paint	Intenal putty work completed, external primer done 55%
		Tiling	Floor Tiling at 17th floor in progress
		Plumbing	Internal water supply and drainage work completed
		Electrical	Conduit work completed, wiring work yet to start
		M.S. Railings	Balcony railing completed and staircase railing in progress
		Internal Plaster	Completed
		External Plaster	88% completed

		Fire Fighting	Internal sprinkler system piping completed
JADE		Brickwork / RMC	Lift shaft brickwork in progress
		Paint	Internal putty work completed, external primer done 50%
		Tiling	Tiling at 18th floor in progress
		Plumbing	Internal water supply and drainage work completed
		Electrical	Conduit work completed, wiring work yet to start
		M.S. Railings	Balcony railing completed and staircase railing in progress
		Internal Plaster	Completed -90%
		External Plaster	82% completed, balance work in progress
		Fire Fighting	Internal sprinkler system piping in progress
AMBER			Structure Work Completed
		Paint	Internal putty work completed, external primer done 62%
		Tiling	Tiling at 20th floor in progress
		Plumbing	Internal water supply and drainage work completed
		Electrical	Conduit work completed, wiring work yet to start
		M.S. Railings	Balcony railing completed and staircase railing in progress
		Internal Plaster	Lift lobby internal plaster - 21st floor
		External Plaster	88% completed
Fire Fighting	Internal sprinkler system piping completed		
SAPPHIRE		RMC	Structure Work Completed
		Paint	Internal putty work completed, external painting done 80%
		Tiling	Lift Wall Tile Cladding at 11th floor completed
		Plumbing	Completed
		Electrical	Conduit work completed, wiring work in progress
		M.S. Railings	Completed
		Internal Plaster	Completed
		External Plaster	Completed
		Fire Fighting	Completed

PEARL		RMC	Structure Work Completed
		Paint	Completed, final coat balance
		Tiling	Completed
		Plumbing	Completed
		Electrical	Completed
		M.S. Railings	Completed
		Internal Plaster	Completed
		External Plaster	Completed
		Fire Fighting	Completed
EMERALD		RMC/Steel	3rd floor roof slab casting - 1st part casted
		Paint	Yet to start
		Tiling	Yet to start
		Plumbing	Yet to start
		Electrical	Yet to start
		M.S. Railings	Yet to start
		Internal Plaster	Yet to start
		External Plaster	N/A
		Fire Fighting	Yet to start
